



Evergreen Epoxy Flooring LLC

METALLIC & DECORATIVE CONCRETE COATINGS

jackalbrecht4@gmail.com · Serving the Skagit Valley & Puget Sound

INVOICE

#1365

Issue date: August 4, 2026

Install window: September 4–8, 2026

BILL TO

Cascadia Eye

Attn: Heidi

1930 Market St, Mount Vernon, WA

(360) 708-6777 · heidim@ncascade.com

PROJECT SITE

Cascadia Eye — Mount Vernon Clinic

1930 Market St, Mount Vernon, WA

Commercial interior · 2,717.75 sq ft total coated area

SCOPE OF WORK & PRICING

Turn-key installation — all prep, materials, labor & equipment included

DESCRIPTION	AREA	RATE	AMOUNT
Metallic Epoxy Floor System Coffee, Silver & Titanium base with Brown Metallic and Copper highlights (Leggari Signature Series—style finish with copper accent). Full system: grinding & removal of existing coating, moisture vapor barrier base coat, hand-worked decorative metallic coat, and high-gloss urethane top coat. <i>Areas: bathroom, nurse station, dilation waiting room, retail/optical room, exit behind front desk, front desk area</i>	2,055.75 sq ft	\$24.00 / sq ft	\$49,338.00
Decorative Flake Floor System Nimbus FB-922 flake blend — blue / misty grey and clean white with subtle brown (no pink). Full system: grinding & removal of existing coating, epoxy base coat with flake broadcast, and polyaspartic top coat. <i>Areas: exam rooms 1–4, laser room, visual fields room</i>	662.00 sq ft	\$10.00 / sq ft	\$6,620.00

Subtotal \$55,958.00

2,000+ sq ft volume discount (20%) –\$11,191.60

Discounted subtotal \$44,766.40

WA sales tax — Mount Vernon (9.0%) \$4,028.98

Total Due \$48,795.38

Deposit (50%) — due to secure install dates \$24,397.69

Balance (50%) — due at final walkthrough \$24,397.69

PAYMENT

Payment by **check** made payable to Evergreen Epoxy Flooring LLC. Card payments are accepted with a 3.5% processing fee (total if paid entirely by card: \$50,503.22).

LIFETIME WARRANTY


This installation includes a **lifetime product warranty** and a **lifetime workmanship warranty**. Full terms are in the attached agreement, ready for signature.

Friday, Sept 4 from 6:00 PM (or earlier if clinic closes early)	Diamond-grind all floors and fully remove the existing coating; prep and detail edges. If the schedule allows, the moisture vapor barrier base coat will also be installed Friday night.
Saturday, Sept 5	Install moisture vapor barrier base coat in the metallic floor areas (if not completed Friday). This seals the slab and ensures long-term adhesion of the decorative metallic system.
Sunday, Sept 6	Install decorative coats — hand-worked metallic (coffee/silver/titanium with brown metallic & copper highlights) in the main areas, and Nimbus FB-922 flake broadcast in the exam, laser, and visual fields rooms.
Monday, Sept 7	Apply top coats — gloss urethane over the metallic floors and polyaspartic over the flake floors. These are the durable, chemical- and scratch-resistant wear layers.
Tuesday, Sept 8	Floor ready for move-back-in. Final walkthrough with Cascadia Eye staff; balance due upon approval. Clinic reopens Wednesday, September 9.

YOUR FLOOR — FINISH REFERENCE



Visualization of the metallic finish rendered in your Cascadia Eye front desk & waiting areas.

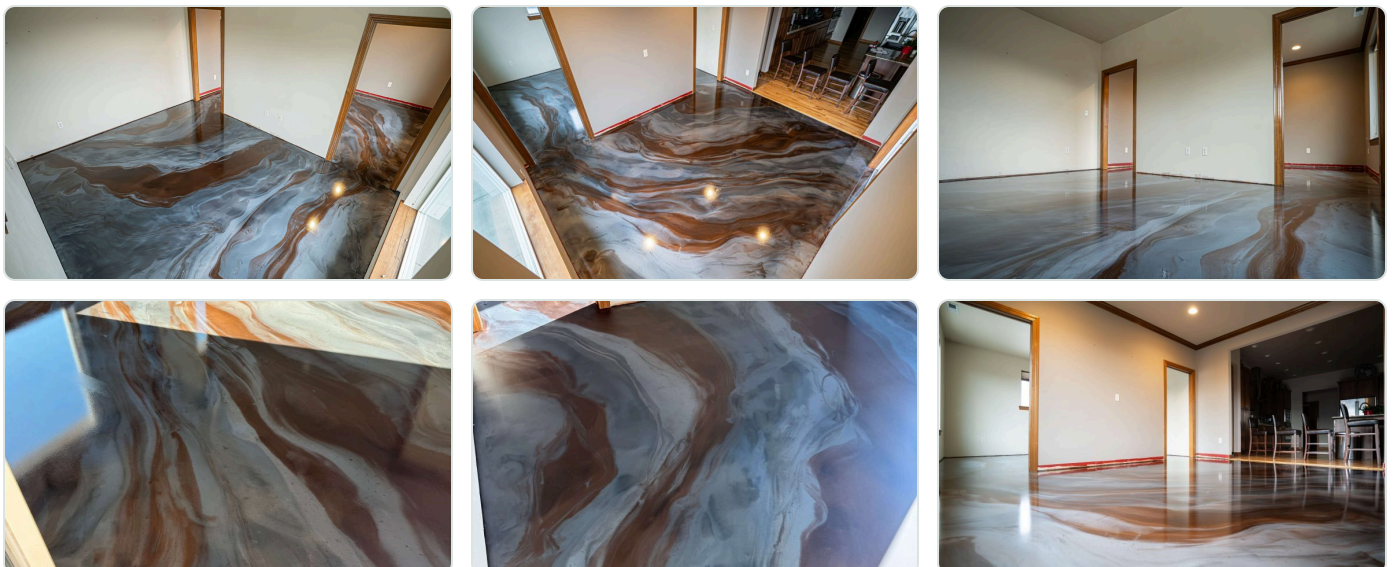

Recent installs of the same coffee / silver / titanium metallic system — your floor will feature added copper highlights.
