



Evergreen Epoxy Flooring LLC

METALLIC & DECORATIVE CONCRETE COATINGS

jackalbrecht4@gmail.com · Serving the Skagit Valley & Puget Sound

INVOICE

#1365

Issue date: August 4, 2026

Install window: September 4–8, 2026

BILL TO

Cascadia Eye

Attn: Heidi
1930 Market St, Mount Vernon, WA
(360) 708-6777 · heidim@ncascade.com

PROJECT SITE

Cascadia Eye — Mount Vernon Clinic

1930 Market St, Mount Vernon, WA
Commercial interior · 2,717.75 sq ft total coated area

SCOPE OF WORK & PRICING

Turn-key installation — all prep, materials, labor & equipment included

DESCRIPTION	AREA	RATE	AMOUNT
Solid Color Epoxy Floor System — Ash Gray Ash Gray solid color — clean, seamless, high-gloss commercial finish. Full system: grinding & removal of existing coating, moisture vapor barrier base coat, full-thickness 100% solids Ash Gray color coat, and high-gloss top coat. <i>Areas: front desk area, waiting/open areas, nurse station, dilation waiting room, retail/optical room, exit behind front desk</i>	1,955.75 sq ft	\$16.00 / sq ft	\$31,292.00
Decorative Flake Floor System Nimbus FB-922 flake blend — blue / misty grey and clean white with subtle brown (no pink). Full system: grinding & removal of existing coating, epoxy base coat with flake broadcast, and polyaspartic top coat. <i>Areas: exam rooms 1–4, laser room, visual fields room, bathroom</i>	762.00 sq ft	\$10.00 / sq ft	\$7,620.00

Subtotal \$38,912.00

Volume discount (20% — flake system) **\$1,524.00**

Discounted subtotal \$37,388.00

WA sales tax — Mount Vernon (9.0%) \$3,364.92

Total Due \$40,752.92

Deposit (50%) — due to secure install dates \$20,376.46

Balance (50%) — due at final walkthrough \$20,376.46

PAYMENT

Payment by **check** payable to Evergreen Epoxy Flooring LLC. Cards accepted with a 3.5% fee (card total: \$42,179.27). Discount applies to flake only — solid color is a full-thickness material pour at our best commercial rate, per consultation.

LIFETIME WARRANTY

This installation includes a **lifetime product warranty** and a **lifetime workmanship warranty**. Full terms are in the attached agreement, ready for signature.

Friday, Sept 4

from 6:00 PM (or earlier if clinic closes early)

Diamond-grind all floors and fully remove the existing coating; prep and detail edges. If the schedule allows, the moisture vapor barrier base coat will also be installed Friday night.

Saturday, Sept 5

Install moisture vapor barrier base coat in the solid color floor areas (if not completed Friday). This seals the slab and ensures long-term adhesion.

Sunday, Sept 6

Install color coats — full-thickness Ash Gray solid color pour in the front desk and open areas, and Nimbus FB-922 flake broadcast in the exam rooms, laser room, visual fields room, and bathroom.

Monday, Sept 7

Apply top coats — high-gloss over the solid color floors and polyaspartic over the flake floors. These are the durable, chemical- and scratch-resistant wear layers.





Tuesday, Sept 8

Floor ready for move-back-in. Final walkthrough with Cascadia Eye staff; balance due upon approval. Clinic reopens Wednesday, September 9.

YOUR FLOOR — FINISH REFERENCE



Visualization of the Ash Gray solid color floor rendered in your Cascadia Eye front desk & waiting areas.

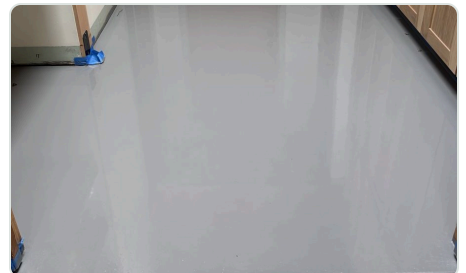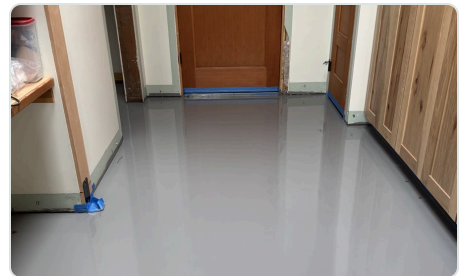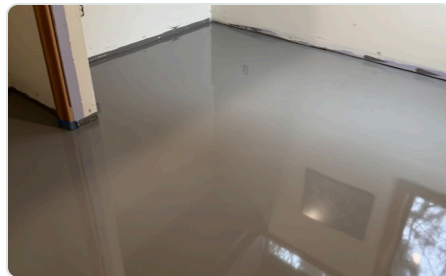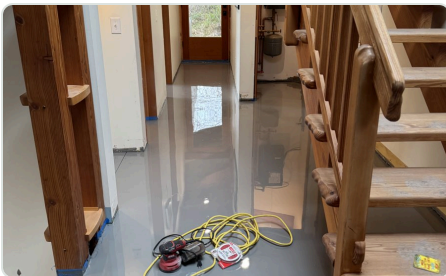

Recent high-gloss solid color installs and your actual Nimbus FB-922 flake sample.
